



Presentation and Discussion Item 8

# RESERVOIRS 1 AND 2 PUMP STATION UPGRADES PROJECT



October 23, 2024

## Reservoir 1 – Site Layout





# Reservoir 2 – Site Layout



3 | October 23, 2024

# Reservoir 2 – Construction



4 | October 23, 2024



# Reservoir 2 – Construction



5 | October 23, 2024



# Reservoir 1 – Construction



6 | October 23, 2024



# Reservoir 1 – Construction



7 | October 23, 2024



# Reservoir Project Schedule


Task	2024				2025				2026	
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
Submittals and Procurement	█	█								
Reservoir 2			█	█	█					
Reservoir 1				█	█	█	█	█	█	
Project Closeout									█	█

8 | October 23, 2024





# Reservoir Project Planned vs. Actual

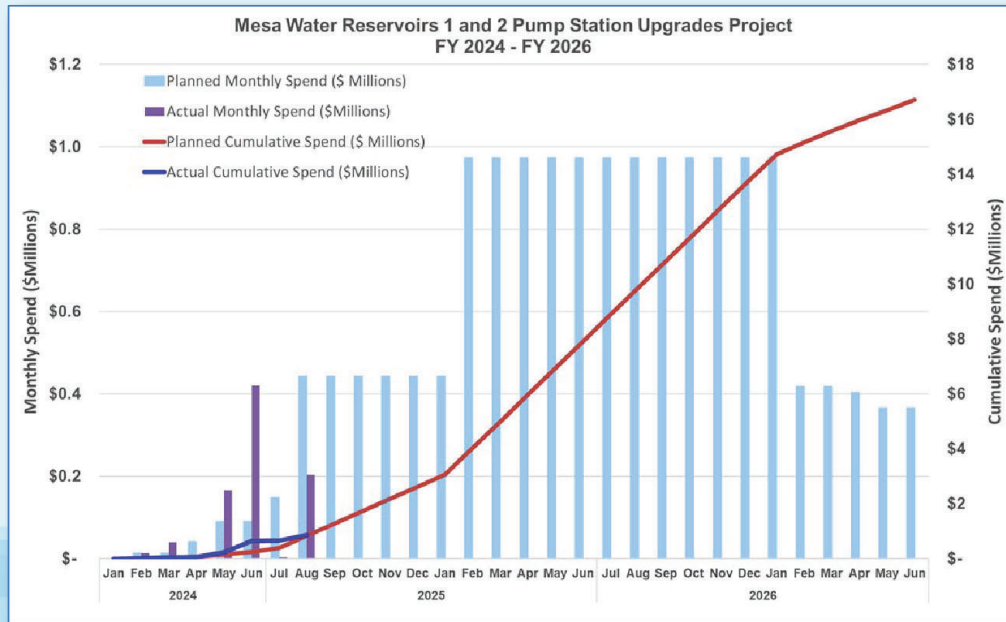

# QUESTIONS?
